


**GRANVILLE - VANCE DISTRICT HEALTH DEPARTMENT
IMPROVEMENT AND OPERATION PERMITS**

COUNTY: <i>Vance</i>	TAX NO. <i>0332 01011</i>	TYPE OF ESTABLISHMENT			*THIS PERMIT SHALL BE ACCOMPANIED BY A LAYOUT SHOWN ON A PLAT, INCLUDING SYSTEM REQUIREMENTS. *THE IMPROVEMENTS PERMIT MUST BE ATTACHED TO A CONSTRUCTION AUTHORIZATION BEFORE OBTAINING BUILDING PERMIT OR OTHER CONSTRUCTION PERMITS AND BEFORE A WASTEWATER SYSTEM IS INSTALLED. *THIS IMPROVEMENT PERMIT IS SUBJECT TO REVOCATION IF THE INTENDED USE CHANGE FROM THOSE SHOWN ON THE IMPROVEMENT PERMIT. CHANGES SHALL REQUIRE HEALTH DEPARTMENT APPROVAL.
	SR NO. <i>1344</i>	RESIDENCE ☒ BUSINESS ☐ OTHER ☐	NUMBER OF BEDROOMS: <i>3</i>	NUMBER OF OCCUPANTS: <i>3</i>	
OWNER: <i>Dana Moore</i>					
APPLICANT: <i>Homeboy Housing</i>		WATER SUPPLY			
APPLICANT'S ADDRESS: <i>3495 US 1 + 158 Henderson</i>		PUBLIC ☐	WELL ☒	OTHER ☐	
PROPERTY ADDRESS/LOCATION: <i>corner of Plum Natty, Plum Natty Rd + Pollyanna 1232</i>		TYPE OF WASTEWATER SYSTEM			
SUBDIVISION: <i>Plum Natty</i>		DESCRIPTION	INITIAL INSTALLATION	REPAIR	
LOT NUMBER: <i>7</i>		DESIGN FLOW:	<i>360 gpm</i>		
REFERENCE SKETCH (SEE PLAT FOR DETAILS) <i>See sketch on back. Dig trenches 18"-24" deep (level) on contour! stay at least 5' from house, 10' from property line + 100' from any well. Do not install or call for inspection in rain.</i>		LTAR:	<i>.4</i>		
		ABSORPTION AREA:	<i>700 sq ft</i>		
		TRENCH WIDTH:	<i>3'</i>		
		TRENCH SPACING:	<i>9' on center</i>		
		TOTAL TRENCH LENGTH:	<i>300 ft</i>		
		NUMBER OF TRENCHES:	<i>2 - (3)</i>		
		GRAVEL DEPTH:	<i>12"</i>		
		TANK SIZE:	<i>1000 gal</i>		
		CONDITIONS:			
IMPROVEMENT PERMIT FOR: <i>Dana Moore / Homeboy Housing</i> ISSUED BY: <i>M.E. Young</i> DATE: <i>4-3-98</i>					
OPERATION PERMIT SYSTEM INSTALLED BY: <i>Lin Cole</i> ISSUED BY: <i>W. Vaughan</i> DATE: <i>5-7-98</i>					

Ellis 1-30-98

11:30

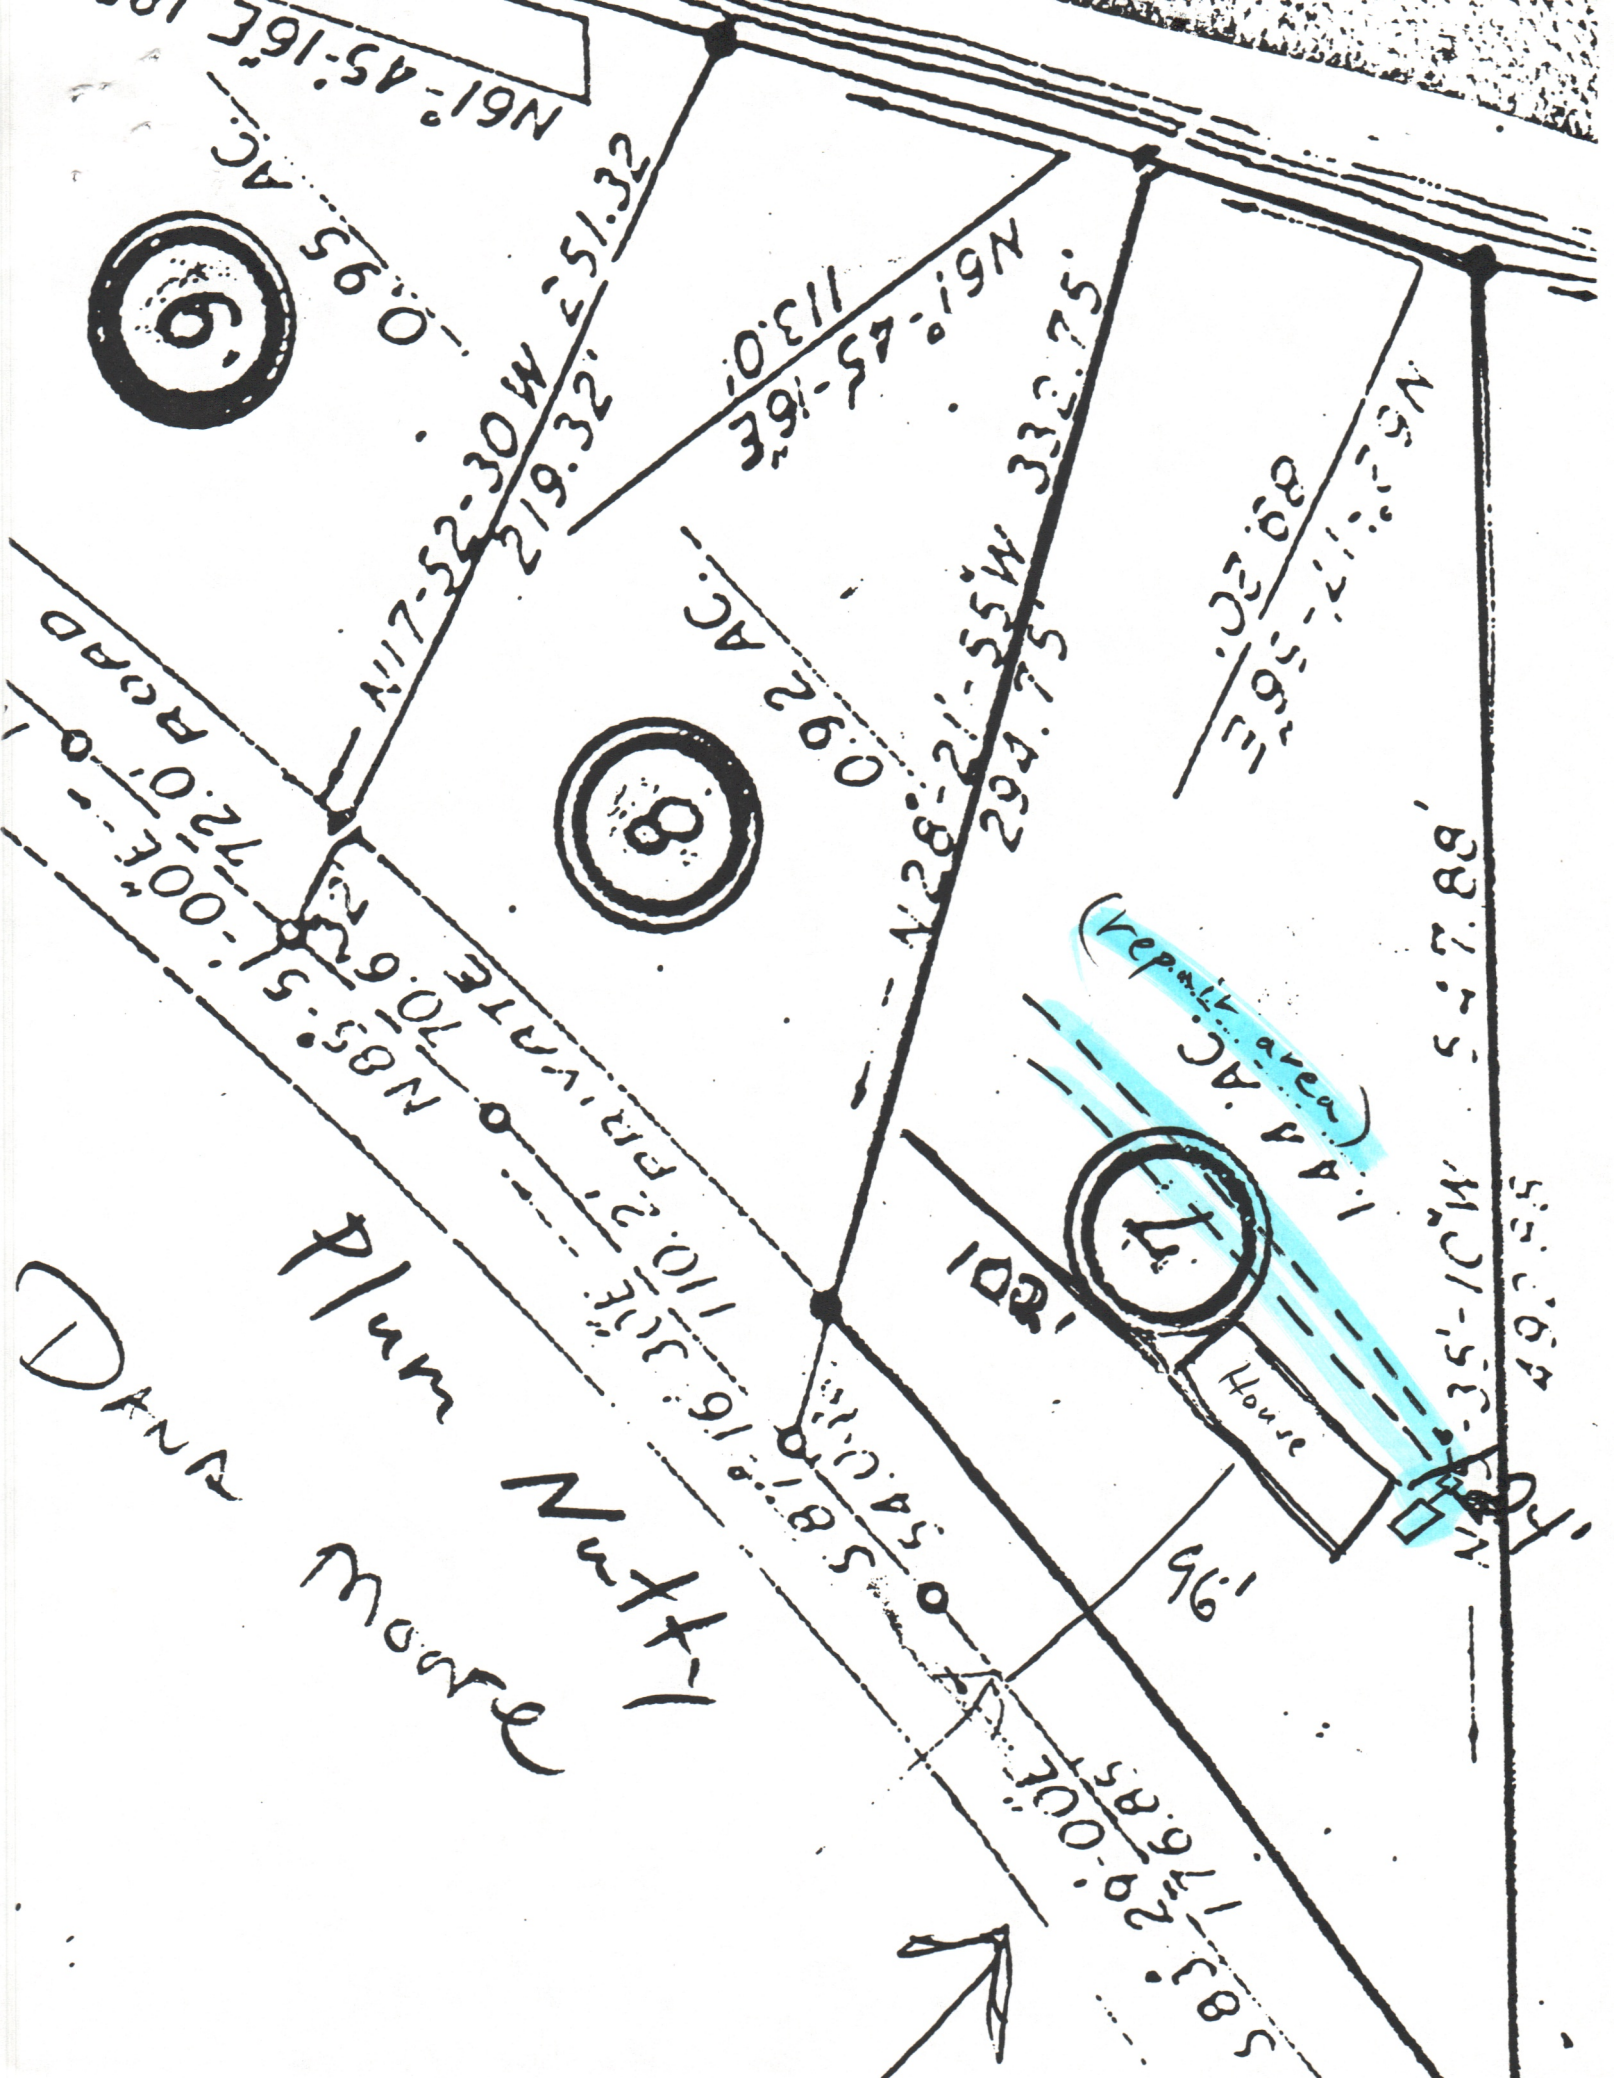

SEWAGE DISPOSAL SYSTEM INSTALLATION REVIEW

OWNER Moore PERMIT NUMBER 1145
 DATE 8-7-98 CONTRACTOR Lin Cole
 WEATHER CONDITIONS cloudy SOIL WETNESS CONDITIONS OK

SEPTIC AND PUMP TANK INSPECTION

SEPTIC TANK	INITIAL	DATE
MANUFACTURER <u>ELC</u>	<u>W.D.</u>	<u>8-7-98</u>
DATE OF MANUFACTURE <u>1-30-98</u>		
STAMP <u>✓</u>		
CAPACITY <u>1000</u>		
TEE <u>✓</u>		
BAFFLE <u>✓</u>		
SEALANT <u>✓</u>		

PUMP TANK		
MANUFACTURER		
DATE OF MANUFACTURE		
STAMP		
CAPACITY		
SEALANT		
MANHOLE		
DRAW DOWN TEST		

MECHANICAL INSPECTION

PUMP		
MANUFACTURER AND MODEL NUMBER		
CONTROL PANEL		
ALARM		
ELECTRICAL CONNECTION		

NITRIFICATION DISTRIBUTION AND DRAINFIELD INSPECTION

DISTRIBUTION BOX		
LEVEL <u>✓</u>		
EQUAL DISTRIBUTION <u>✓</u>		
OTHER		

DISTRIBUTION MANIFOLD		
PIPE SIZE		
GATE VALVES		
OTHER		

OTHER DISTRIBUTION TYPE		
-------------------------	--	--

NITRIFICATION LINES	LINE 1	LINE 2	LINE 3		
TRENCH WIDTH	<u>3</u>	<u>3</u>	<u>3</u>		
TRENCH LENGTH	<u>100</u>	<u>100</u>	<u>100</u>		
TRENCH GRADE	<u>1/2</u>	<u>1/2</u>	<u>1/2</u>		
STONE DEPTH	<u>12</u>	<u>12</u>	<u>12</u>		

COMMENTS: _____

