

Environmental Services - Water Quality
Onsite Wastewater Scan Data Entry Form

PERMIT #: C 0 2 0 6 8 0

PIN #: 1 8 0 0 9 5 7 0 7 1

OP DATE: 0 8 1 0 2 1 1 9 9 5

SYSTEM USE:

- ☒ House
☐ Mobile Home
☐ Business
☐ Other

SEWAGE TYPE:

- ☒ Domestic
☐ Industrial

PUMP/SIPHON?:

- ☒ Yes
☐ No

PRESSURE MANIFOLD:

- ☐ Yes
☒ No

SYSTEM TYPE:

- ☐ I
☐ II
☒ III
☐ IV
☐ V
☐ VI
☐ Other

SUB TYPE:

- ☐ A
☒ B
☐ C
☐ D
☐ E
☐ F
☐ G

NBR BEDROOMS:

- ☐ 1
☐ 2
☐ 3
☒ 4
☐ 5
☐ 6
☐ Other

MAINT. SCHEDULE:

- ☐ Yes
☒ No

CERT. OPERATOR

- ☐ Yes
☒ No

GT ST PT

- ☐ ☐ ☐
☐ ☐ ☐
☐ ☐ ☐
☐ ☒ ☒
☐ ☐ ☐
☐ ☐ ☐
☐ ☐ ☐
☐ ☐ ☐
☐ ☐ ☐
☐ ☐ ☐
☐ ☐ ☐
☐ ☐ ☐
☐ ☐ ☐
☒ ☐ ☐

SIZE

- 750
900
1,000
1,200
1,500
1,800
2,100
2,500
3,000
4,000
5,000
8,000
10,000
Other
None/NA GT or PT

DRAINFIELD SIZE(SQ. FT.)

0 1 2 0 0

DRAIN TYPE:

- ☒ Stone
☐ EZ Flow
☐ Infiltrator
☐ Biodiffuser
☐ Cultec
☐ Drip
☐ Hancor
☐ Large Dia. Pipe
☐ Multi-Pipe
☐ Other

MAX DEPTH (IN.):

- ☐ 12 in. or less
☐ 18 in. or less
☐ 24 in. or less
☐ 26 in. or less
☐ 28 in. or less
☒ 30 in. or less
☐ 32 in. or less
☐ 36 in. or less
☐ Other

STONE DEPTH (IN.):

- ☐ 8 in. or less
☒ 12 in. or less
☐ 18 in. or less
☐ 24 in. or less
☐ Other

TRENCHES:

- ☒ Individual
☐ Bed

TRENCH WIDTH (IN.):

- ☐ 12 in. or less
☐ 18 in.
☐ 24 in.
☒ 36 in.
☐ 6 ft. or less
☐ 9 ft. or less
☐ Other

WAKE COUNTY HEALTH DEPARTMENT WELL AND SEWAGE SITE, LOCATION PERMIT

ALL PERMITS VOID 60 MONTHS FROM DATE OF ISSUANCE

Pin # 1800.02957071 Project # 0944057

Tax Map No. 028 Parcel No. ---

Zoning Wake Township Barton's Creek

Owner/Contractor: Tommy Oates

Improvement Permit

Well Permit No. **C 20680**

Operation Permit []

Date: 7-7-94

Location/Address: (1105 Ekin's Way) Six Forks N, straight on Bayleaf Ch.
(R) 510, lot on Left.

S.R. # 2002

Subdivision Name: Avanlea

Lot No. 4

Section or Block No. ---

Preliminary Layout

Final Layout



Sewage System Specifications

Repair [] Original Permit No. ---

Garbage Disposal Unit Yes [] No [4]

House [4] Mobile Home [] Business []

No. of Bedrooms 4 Lot Area 2.52

Size of Tank 1200ST 1200 PT gal.

*Comments: Keep system shallow! Follow contour, keep well 50' min. from house & 10 min. from prop. line. 9-21-94 now site plan, pump system

Date: 8-2-95 Installed By: Cole Brothers

Nitrification Line 1200' 4" (3' x 200') sq. ft.

Depth of Stone: 12" Max Depth of Trenches: 30 in.

Riser and Baffle Required [4] Pump Required []

Permit void if not in compliance with zoning regulations

Permits may be voided if site is altered or intended use changed

Layout by: Terry D. Chappell R.S.

Well System
Individual [4] Semi-Public [] Public []
New [4] Replacement [] Repair []
Fee Paid: Yes [4] No []

Construction Compliance
Site Approved [4]
Well Head Approved [4]
Grouting Approved [4]
Date Inspected 5-23-95 Sanitarian Ralph McDonald R.S.

Bacteriological Results
Initial Sample: absent Date: 7-31-95
* Re-Sample #1 _____ Date: _____
* Re-Sample #2 _____ Date: _____
* Re-chlorination as required [] Yes [] No
* Fees for all resamples
All checks payable to: **Wake County Health Department**

Final Inspection
Required Slab [4]
Chlorinated [4]
Required Certificate []
Variance (Explain) []
WCHD I.D. Affixed 5540 [4]
Sample Collected [4]


Comments: _____

Well Installed By: Ralph McDonald
8-2-95 Date System Finalized
Sanitarian Ralph McDonald R.S.

This report is based in part on information provided by the homeowner or his/her representative in the application submitted for this permit. The sanitarian is not responsible for false or misleading information contained in the application. The sanitarian is also not responsible for concealed conditions on the property or for statements in this report that may have resulted from false or misleading statements provided to him in the application. Neither Wake County nor the sanitarian warrants that the septic tank system will continue to function satisfactorily in the future or that the water supply will remain potable.

COPY TO HEALTH DEPARTMENT

3002.017 - 5/14/93

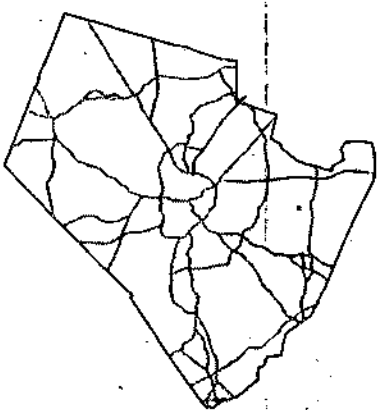

7/28/2010 3:21 PM



Site plan approved as shown for Geothermal Closed Loop Pit.
Any changes to site plan voids approval. All setbacks apply
for septic systems and wells, regarding any pools, decks,
additions and/or accessory structures. Applicant is responsible
for protecting all portions of the septic system, repair area and
wells from damage during construction. Adhere to all Local and
State Rules.
Approved by Shawn A. Hovson Date 7/28/10
Wake County Department of Environmental Services.
Water and Waste Water Section

This document is a graphic representation only,
created from the best available sources.
Wake County assumes no responsibility for any errors,
or misuse of this document.

Wake County
Environmental Services
(919) 856-7400
<http://www.wakegov.com>

