

242 ~~181~~


2:30 - 3:00

Wed. Sept

PERMIT NUMBER N2 301

GRANVILLE - VANCE DISTRICT HEALTH DEPARTMENT IMPROVEMENT AND OPERATION PERMITS

COUNTY:	TAX NO.	TYPE OF ESTABLISHMENT			*THIS PERMIT SHALL BE ACCOMPANIED BY A LAYOUT SHOWN ON A PLAT, INCLUDING SYSTEM REQUIREMENTS.
Granville	SR NO. 1308	RESIDENCE ☒	NUMBER OF BEDROOMS: 3	NUMBER OF OCCUPANTS: 2	
OWNER: David Jones		BUSINESS ☐			
		OTHER ☐			
APPLICANT: David Jones		WATER SUPPLY			*THE IMPROVEMENTS PERMIT MUST BE ATTACHED TO A CONSTRUCTION AUTHORIZATION BEFORE OBTAINING BUILDING PERMIT OR OTHER CONSTRUCTION PERMITS AND BEFORE A WASTEWATER SYSTEM IS INSTALLED.
APPLICANT'S ADDRESS: Durham, NC 27703 825 Carter Ave.		PUBLIC ☐	WELL ☒	OTHER ☐	
PROPERTY ADDRESS/LOCATION: End of Dean Road		TYPE OF WASTEWATER SYSTEM			
		DESCRIPTION	INITIAL ☒ INSTALLATION	REPAIR	
SUBDIVISION:	DESIGN FLOW:	360 gal/day			*THIS IMPROVEMENT PERMIT IS SUBJECT TO REVOCATION IF THE INTENDED USE CHANGE FROM THOSE SHOWN ON THE IMPROVEMENT PERMIT. CHANGES SHALL REQUIRE HEALTH DEPARTMENT APPROVAL.
LOT NUMBER:	LTAR:	.4			
REFERENCE SKETCH (SEE PLAT FOR DETAILS) See sketch attached. Dig trenches on contours (level) 18" - 24" deep. Stay 5' from house, 10' from property line, & 100' from any well. Stay out of flood plain	ABSORPTION AREA:	900 sq. ft.			
	TRENCH WIDTH:	3'			
	TRENCH SPACING:	9' on center			
	TOTAL TRENCH LENGTH:	300'			
	NUMBER OF TRENCHES:	2 or 3			
	GRAVEL DEPTH:	12"			
TANK SIZE:	900 gal.				
CONDITIONS:					
IMPROVEMENT PERMIT		DATE:			
FOR: David Jones	8-5-96				
ISSUED BY: M.E. Yount					
OPERATION PERMIT		DATE:			
SYSTEM INSTALLED BY: Cole's Backhoe Service	9-18-96				
ISSUED BY: M.E. Yount					

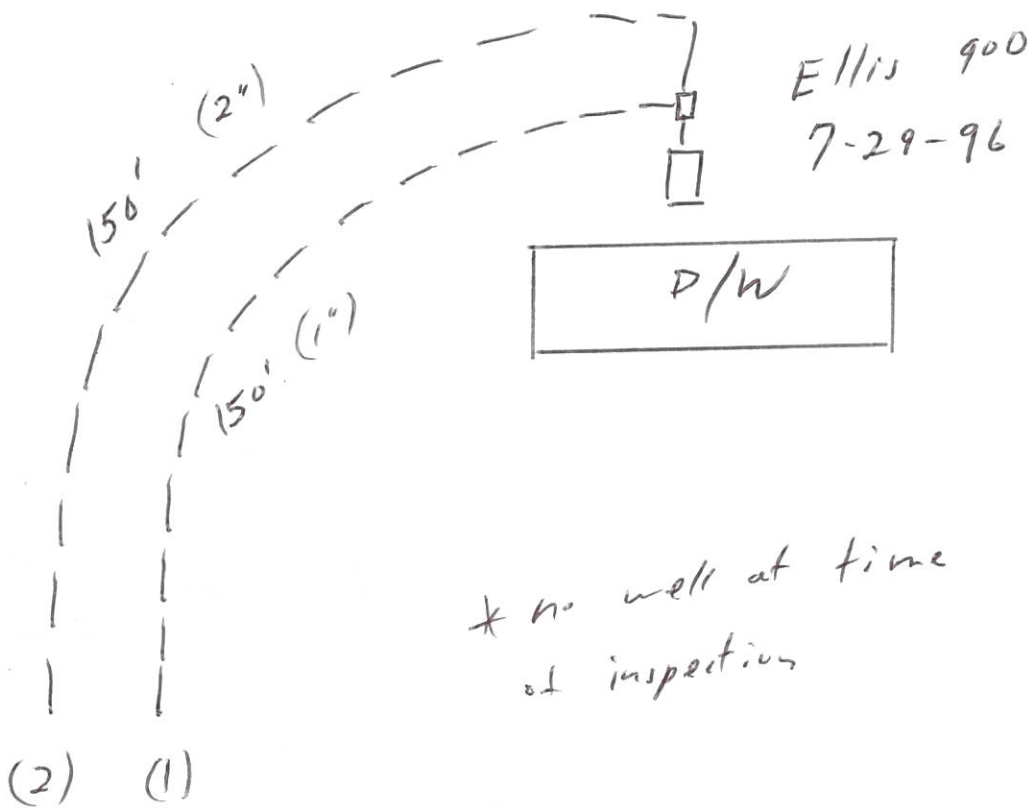

Drive

✓
Dean Road
J.R. 1308
