

Environmental Services - Water Quality
Onsite Wastewater Scan Data Entry Form

PERMIT #:

PIN #:

OP DATE:

SYSTEM USE:

- ☒ House
☐ Mobile Home
☐ Business
☐ Other

SEWAGE TYPE:

- ☒ Domestic
☐ Industrial

PUMP/SIPHON?:

- ☐ Yes
☒ No

PRESSURE MANIFOLD:

- ☐ Yes
☒ No

SYSTEM TYPE:

- ☐ I
☒ II
☐ III
☐ IV
☐ V
☐ VI
☐ Other

SUB TYPE:

- ☒ A
☐ B
☐ C
☐ D
☐ E
☐ F
☐ G

NBR BEDROOMS:

- ☐ 1
☐ 2
☐ 3
☒ 4
☐ 5
☐ 6
☐ Other

MAINT. SCHEDULE:

- ☐ Yes
☒ No

CERT. OPERATOR

- ☐ Yes
☒ No

GT ST PT SIZE

- | | | | |
|-------------------------------------|-------------------------------------|-------------------------------------|------------------|
| ☐ | ☐ | | 750 |
| ☐ | ☐ | ☐ | 900 |
| ☐ | ☐ | ☐ | 1,000 |
| ☐ | ☒ | ☐ | 1,200 |
| ☐ | ☐ | ☐ | 1,500 |
| ☐ | ☐ | ☐ | 1,800 |
| ☐ | ☐ | ☐ | 2,100 |
| ☐ | ☐ | ☐ | 2,500 |
| ☐ | ☐ | ☐ | 3,000 |
| ☐ | ☐ | ☐ | 4,000 |
| ☐ | ☐ | ☐ | 5,000 |
| ☐ | ☐ | ☐ | 8,000 |
| ☐ | ☐ | ☐ | 10,000 |
| ☐ | ☐ | ☐ | Other |
| ☒ | | ☒ | None/NA GT or PT |

DRAINFIELD SIZE(SQ. FT.)

DRAIN TYPE:

- ☒ Stone
☐ EZ Flow
☐ Infiltrator
☐ Biodiffuser
☐ Cultec
☐ Drip
☐ Hancor
☐ Large Dia. Pipe
☐ Multi-Pipe
☐ Other

MAX DEPTH (IN.):

- ☐ 12 in. or less
☐ 18 in. or less
☒ 24 in. or less
☐ 26 in. or less
☐ 28 in. or less
☐ 30 in. or less
☐ 32 in. or less
☐ 36 in. or less
☐ Other

STONE DEPTH (IN.):

- ☐ 8 in. or less
☒ 12 in. or less
☐ 18 in. or less
☐ 24 in. or less
☐ Other

TRENCHES:

- ☒ Individual
☐ Bed

TRENCH WIDTH (IN.):

- ☐ 12 in. or less
☐ 18 in.
☒ 24 in.
☐ 36 in.
☐ 6 ft. or less
☐ 9 ft. or less
☐ Other

B.W. 10/20/14



WAKE COUNTY HEALTH DEPARTMENT WELL AND SEWAGE SITE, LOCATION PERMIT

ALL PERMITS VOID 60 MONTHS FROM DATE OF ISSUANCE

Pin # 1708.02676115 Project # 952634
 Tax Map No. 282 Parcel No.
 Zoning Wake Township Barton's Creek
 Owner/Contractor: Massengill + Blue Stone Inc
 Location/Address: 1017 Bearslake Ln.

Improvement Permit
 Well Permit No. **C 23418**
 Operation Permit []
 Date: 3-14-95

Location/Address: Durham Rd (TL) into Sub. to Bearslake S.R. #
 Subdivision Name: Cross Gate Lot No. 109 Section or Block No.

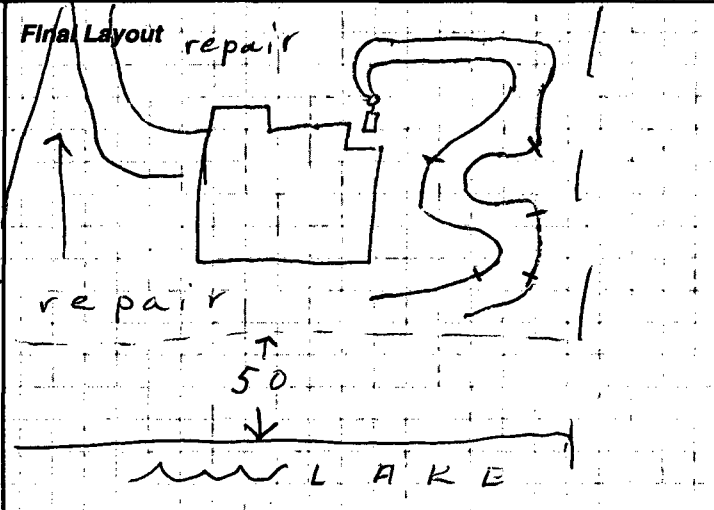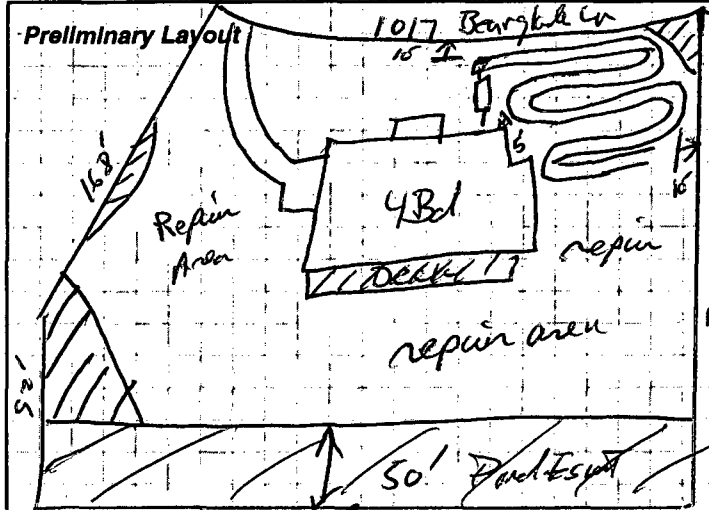

Sewage System Specifications
 Repair [] Original Permit No.
 Garbage Disposal Unit Yes [] No ☒
 House ☒ Mobile Home [] Business []
 No. of Bedrooms 4 Lot Area 1.35 AC
 Size of Tank 1200 gal.

Nitrification Line 2x3x225 = 1350 sq. ft.
 Depth of Stone: 12" ☒ Max Depth of Trenches: 24 in.
 Riser and Baffle Required ☒ Pump Required []
 Permit void if not in compliance with zoning regulations
 Permits may be voided if site is altered or intended use changed
 Layout by: Kent D. Dade

Comments: Use as much of front yard as possible for trench, 5' to off prop line
5' off House, keep system out of any altered site
 Date: 3/13/95 Installed By: GSTR Approved By: JR Parnell

Well System
 Individual [] Semi-Public [] Public ☒
 New [] Replacement [] Repair []
 Fee Paid: Yes [] No []
 Construction Compliance Yes No
 Site Approved [] []
 Well Head Approved [] []
 Grouting Approved [] []

Final Inspection

	Yes	No
Required Slab	[]	[]
Chlorinated	[]	[]
Required Certificate	[]	[]
Variance (Explain)	[]	[]
WCHD I.D. Affixed	[]	[]
Sample Collected	[]	[]

Date Inspected: Sanitarian
Bacteriological Results
 Initial Sample: Date:
 * Re-Sample #1 Date:
 * Re-Sample #2 Date:
 * Re-chlorination as required [] Yes [] No
 * Fees for all resamples
 All checks payable to: **Wake County Health Department**

Comments:

 Well Installed By:
 Date System Finalized Sanitarian

This report is based in part on information provided by the homeowner or his/her representative in the application submitted for this permit. The sanitarian is not responsible for false or misleading information contained in the application. The sanitarian is also not responsible for concealed conditions on the property or for statements in this report that may have resulted from false or misleading statements provided to him in the application. Neither Wake County nor the sanitarian warrants that the septic tank system will continue to function satisfactorily in the future or that the water supply will remain potable.
