

GRANVILLE-VANCE HEALTH DEPARTMENT—Sewage Disposal Record

Owner or Contractor Brent Brewer / Dr. Clyde Caldwell Date 8-5-99 S.R. No. 1662
 Location/Address Tabbs Creek Lane + Beechwood Hill
 Subdivision/Mobile Home Park Name 5224 Beechwood Hill Ct. Lot Size 1.85 acres
 Permit No. # 1730 Lot No. 6

New System ☒ Repair _____
 House ☒ Mobile Home _____ Business _____
 No. Bedrooms 3 No. People _____ No. Toilets _____
 Water Supply: Private ☒ Approved _____
 Semi-Public _____ Unapproved _____
 Public _____ None _____

Nitrification System:


Tank Size 1000 gal.
 Distribution Box ☒ No. Lines 4
 Nitrification Field 1050 Sq. Ft.
 Lines: 1 2 3 4 5 6
 Width 3' 3' 3' 3' _____ _____
 Length 100' 100' 100' 100' _____ _____
 Grade 0" 0" 0" 0" _____ _____
 Stone Depth 12" 12" 12" 12" _____ _____

Layout to be followed by installer:

Improvements Permit By Chris Hedrick Installer Cole's Backhoe Service
 Certificate of Completion By Eddie Yount Date of Inspection 8-5-99

* Construction must comply with all other applicable state and local regulations, but the permit is not a guarantee that the system will not malfunction and the Granville-Vance Health District will not be held responsible for a malfunctioning system.

NOTE: Make sketch of installation showing location of house, septic tanks, privies, water supplies on adjacent property, etc. Write in measurements in order that installations may be located at later date.

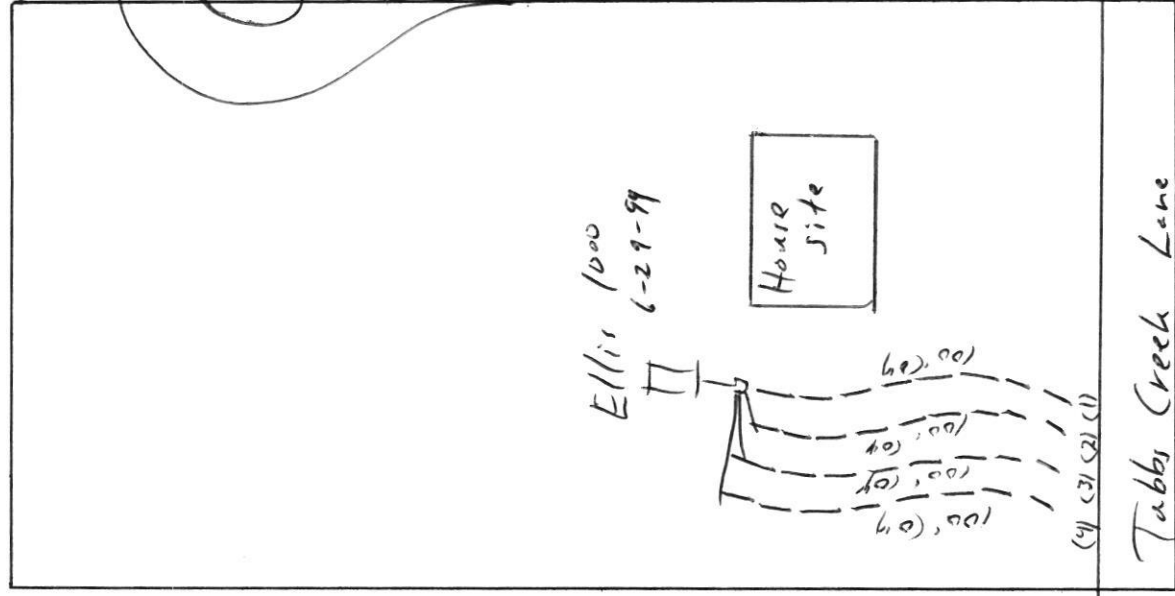

SEWAGE DISPOSAL SYSTEM INSTALLATION REVIEW

OWNER Dr. Clyde & Cathy Caldwell PERMIT NUMBER 1730
 DATE 8-5-99 CONTRACTOR Cole's Backhoe Service
 WEATHER CONDITIONS Sunny Hot SOIL WETNESS CONDITIONS Dry

SEPTIC AND PUMP TANK INSPECTION

SEPTIC TANK		INITIAL	DATE
MANUFACTURER	<u>Ellis</u>	<u>MSB</u>	<u>8-5-99</u>
DATE OF MANUFACTURE	<u>6-29-99</u>		
STAMP			
CAPACITY	<u>yes</u> <u>1000</u>		
TEE	<u>yes</u>		
BAFFLE	<u>yes</u>		
SEALANT	<u>yes</u>		
<u>Air gap yes, Filter yes, Muck yes</u>			
PUMP TANK			
MANUFACTURER			
DATE OF MANUFACTURE			
STAMP			
CAPACITY			
SEALANT			
MANHOLE			
DRAW DOWN TEST			

MECHANICAL INSPECTION

PUMP			
MANUFACTURER AND MODEL NUMBER			
CONTROL PANEL			
ALARM			
ELECTRICAL CONNECTION			

NITRIFICATION DISTRIBUTION AND DRAINFIELD INSPECTION

DISTRIBUTION BOX			
LEVEL	<u>yes</u>	<u>MSB</u>	<u>8-5-99</u>
EQUAL DISTRIBUTION	<u>yes</u>		
OTHER			


DISTRIBUTION MANIFOLD			
PIPE SIZE			
GATE VALVES			
OTHER			

OTHER DISTRIBUTION TYPE			

NITRIFICATION LINES	LINE 1	LINE 2	LINE 3		
TRENCH WIDTH	<u>3'</u>	<u>3'</u>	<u>3'</u>	<u>3'</u>	<u>MSB 8-5-99</u>
TRENCH LENGTH	<u>100'</u>	<u>100'</u>	<u>100'</u>	<u>100'</u>	
TRENCH GRADE	<u>6"</u>	<u>0"</u>	<u>0"</u>	<u>0"</u>	
STONE DEPTH	<u>12"</u>	<u>12"</u>	<u>12"</u>	<u>12"</u>	

COMMENTS: _____

Stream

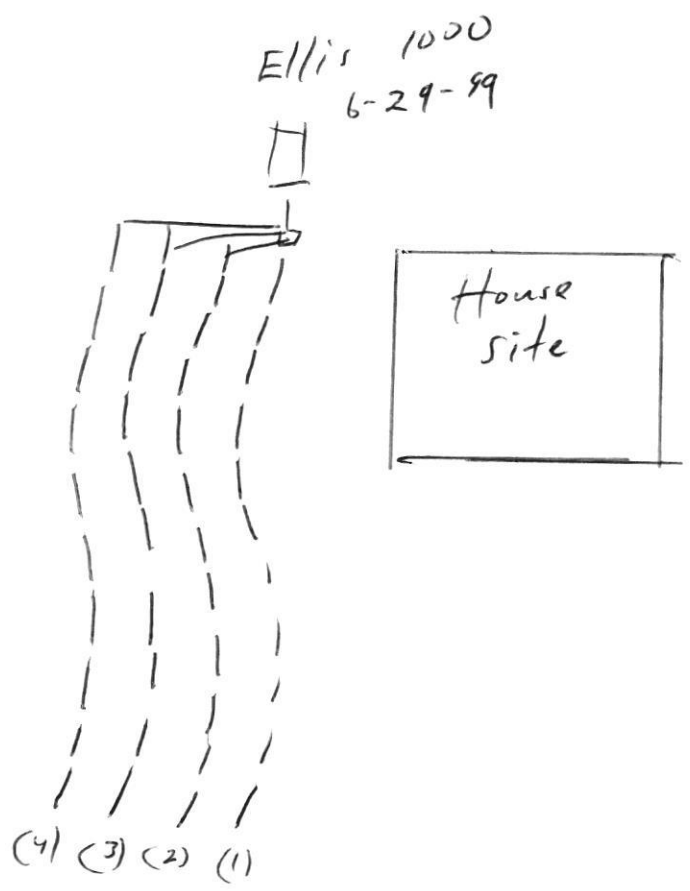

Beachwood Hill

US 158


Tabbs Creek Lane

2:00 Lin Cole

PERMIT NUMBER 192 1730

5224 Beechwood Hill Ct

GRANVILLE - VANCE DISTRICT HEALTH DEPARTMENT
IMPROVEMENT AND OPERATION PERMITS

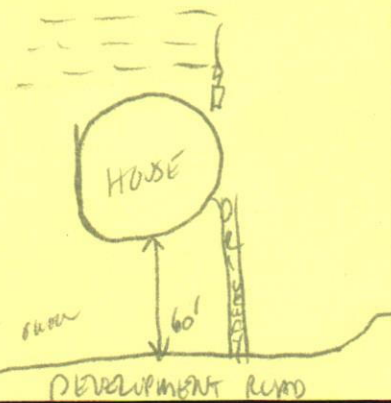COUNTY:	TAX NO. ~~193301762171~~	TYPE OF ESTABLISHMENT <u>193304703191</u>			*THIS PERMIT SHALL BE ACCOMPANIED BY A LAYOUT SHOWN ON A PLAT, INCLUDING SYSTEM REQUIREMENTS.
Granville	SIR NO. <u>1662</u>	RESIDENCE ☒	NUMBER OF BEDROOMS:	NUMBER OF OCCUPANTS:	
OWNER:		BUSINESS ☐			
		OTHER ☐	<u>3</u>	<u>2</u>	
APPLICANT:		WATER SUPPLY			*THE IMPROVEMENTS PERMIT MUST BE ATTACHED TO A CONSTRUCTION AUTHORIZATION BEFORE OBTAINING BUILDING PERMIT OR OTHER CONSTRUCTION PERMITS AND BEFORE A WASTEWATER SYSTEM IS INSTALLED.
Dr. Clyde & Cathy Coldwell					
APPLICANT'S ADDRESS:		PUBLIC ☐	WELL ☒	OTHER ☐	
PROPERTY ADDRESS/LOCATION:		TYPE OF WASTEWATER SYSTEM			*THIS IMPROVEMENT PERMIT IS SUBJECT TO REVOCATION IF THE INTENDED USE CHANGE FROM THOSE SHOWN ON THE IMPROVEMENT PERMIT. CHANGES SHALL REQUIRE HEALTH DEPARTMENT APPROVAL.
Tobbs Creek Lane.		DESCRIPTION	INITIAL INSTALLATION	REPAIR	
SUBDIVISION:		DESIGN FLOW:	<u>300 Gallons/Day</u>		
LOT NUMBER:		LTAR:	<u>0.35 Gallons/Day/ft²</u>		
REFERENCE SKETCH (SEE PLAT FOR DETAILS)		ABSORPTION AREA:	<u>1050 ft²</u>		
		TRENCH WIDTH:	<u>3'</u>		
		TRENCH SPACING:	<u>4' or Center</u>		
		TOTAL TRENCH LENGTH:	<u>350'</u>		
		NUMBER OF TRENCHES:	<u>3</u>		
		GRAVEL DEPTH:	<u>12"</u>		
		TANK SIZE:	<u>1000 Gallons + D</u>		
		CONDITIONS:	<u>See Attachment to Case +</u>		
IMPROVEMENT PERMIT				DATE:	
FOR: <u>Clyde + Cathy Coldwell</u>				<u>2-5-99</u>	
ISSUED BY: <u>Chris Hedera</u>					
OPERATION PERMIT				DATE:	
SYSTEM INSTALLED BY: <u>Cole's Backhoe Service</u>				<u>8-5-99</u>	
ISSUED BY: <u>M.E. Young Jr</u>					

1330

100-4-1015

2004 December 1st

175-175

11-11-11
11-11-11
11-11-11
